

## Temporary half-pipe ramp — temporary works report

20.00 m long, 5.00 m of riding surface, 2.00 m coping. Wind check, hold-down demand, priced build sheet and 3D model.

|                |                |            |           |
|----------------|----------------|------------|-----------|
| Prepared for   | Date           | Status     | Reference |
| Darren Hopwood | 4 October 2026 | For review | TW-HP-001 |

### 01 What this is, and what it is not

Read before anything else in the pack.

#### NOT A DESIGN. NOT FOR CONSTRUCTION. NOT A PERMIT TO LOAD OR RIDE.

The wind pressure is calculated here and every step is shown. The **structure is not designed here** - not the transitions, not the connections, not the dynamic load a skateboarder puts into it.

The design and its independent check must be produced, checked and owned by a competent temporary works designer. Nothing is erected, ballasted or ridden until a permit to load has been issued.

What it does give you is the number that decides the job: the ramp is a **40 m<sup>2</sup> sail**, and it has to be held down.

### 02 The structure

Geometry adopted from the brief, with the arithmetic shown.

The brief was "20 m x 5 m". That splits exactly: a **1.00 m flat bottom** and two **2.00 m transitions** make the 5.00 m riding surface, so the coping stands **2.00 m** high with a 2.00 m radius. Decks 0.60 m each side give a 6.20 m overall footprint.

| ELEMENT           | DESIGN INTENT                                                                                        |
|-------------------|------------------------------------------------------------------------------------------------------|
| Length            | 20.00 m                                                                                              |
| Riding surface    | 5.00 m — 1.00 m flat + two 2.00 m transitions                                                        |
| Coping height     | 2.00 m                                                                                               |
| Overall footprint | 20.00 m x 6.20 m including decks                                                                     |
| Framing           | 100 × 100 C24 legs on 450 × 450 pads, 100 × 75 bearers, curved ply ribs at 1.20 m centres, 18 frames |
| Surface           | 24 mm ply in two layers, 18 mm ply closing the sides and ends                                        |
| Coping            | 60 mm steel tube, both edges, 40 m total                                                             |

| ELEMENT   | DESIGN INTENT                              |
|-----------|--------------------------------------------|
| Hold-down | Ballast or ground anchors — see section 03 |

### 03 The engineering — wind, and what it means

This is the point of the pack.

Dynamic pressure is  $q_p = 0.613 \times c_{prob}^2 \times C_{ef} \times S_{wind}^2$ .  $S_{wind}$  and  $C_{ef}$  come from the validated calculator that reproduces the published TWf2012:01 worked example. Those two are properties of the **site and the height**, so they carry across to a ramp. The hoarding's shape coefficients do not, and are not used.

The site is not confirmed, so the pressure is shown as a range and the designer locks the row.

| VB,MAP | FROM SEA | CEF   | SWIND M/S | QP KN/M² |
|--------|----------|-------|-----------|----------|
| 22 m/s | 2 km     | 1.070 | 22.44     | 0.330    |
| 22 m/s | 30 km    | 0.994 | 22.44     | 0.307    |
| 25 m/s | 2 km     | 1.070 | 25.50     | 0.427    |
| 25 m/s | 30 km    | 0.994 | 25.50     | 0.396    |

#### The hold-down demand

The ramp shows a **40 m²** side elevation to a cross wind. The shape factor is **not taken from any standard I hold** — it is assumed and carried as a sensitivity, so the designer can price their own figure.

| CF ASSUMED | WIND FORCE | SLIDING RESISTANCE NEEDED AT M 0.30 | EXTRA BALLAST NEEDED |
|------------|------------|-------------------------------------|----------------------|
| 1.0        | 18.7 kN    | 62.4 kN                             | 3.0 t                |
| 1.3        | 24.3 kN    | 81.1 kN                             | 4.9 t                |
| 1.6        | 30.0 kN    | 99.8 kN                             | 6.8 t                |

**The commercial headline.** Self weight is about 3.4 t, which resists roughly 10 kN on its own. Against a wind force of 19 to 30 kN, **the ramp needs holding down in every case** — ballast in the order of **3 to 7 tonnes**, or ground anchors. Fixing that early is the difference between an event that runs and one that does not.

**Not checked here, and must be:** uplift (a trough is open on top, so wind over the opening can lift the surface), the dynamic load of a rider landing, and every structural member and connection. All of that belongs to the designer.

## 04 The standards that govern it

Checked, not remembered.

| DOCUMENT                               | WHAT IT COVERS                                                                                                                                                                           |
|----------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>BS EN 14974:2019</b>                | Skateparks - safety requirements and test methods. THE product standard for a facility used by the public on skateboards, roller sports and BMX. Supersedes BS EN 14974:2006+A1:2010.    |
| <b>BS EN 13814-1:2019+A1:2024</b>      | Safety of amusement rides and amusement devices - design and manufacture. Applies to mobile and temporary devices: if the ramp is hired in as an attraction this is the design standard. |
| <b>BS EN 1991-1-4</b>                  | Wind actions, where the designer works to Eurocode rather than the simplified method.                                                                                                    |
| <b>BS 5975-1:2024 / BS 5975-2:2024</b> | Temporary works procedure: roles, register, check categories, permits. Replaced BS 5975:2019.                                                                                            |
| <b>CDM 2015</b>                        | Principal Contractor duties, the design brief, and the temporary works register.                                                                                                         |
| <b>BS EN 1090-1</b>                    | Execution of steel structures - if the coping, anchors or frame are fabricated steel.                                                                                                    |

## 05 The money

Measured quantities at building rates. Every line noted.

| ITEM                                                       | QUANTITY  | RATE    | AMOUNT    |
|------------------------------------------------------------|-----------|---------|-----------|
| <b>A. TIMBER</b>                                           |           |         |           |
| Leg 100 × 100 C24 treated, average 1.50 m                  | 36 no     | £16.50  | £594.00   |
| Bearer / rail 100 × 75 C24 treated, laid flat              | 180 m     | £8.20   | £1,476.00 |
| Cross bearer under the flat, 100 × 75                      | 27 m      | £8.20   | £221.40   |
| <b>B. PLY</b>                                              |           |         |           |
| Ply 12 mm exterior, riding surface, two layers             | 115 sheet | £38.00  | £4,370.00 |
| Ply 18 mm exterior, side and end closing                   | 26 sheet  | £46.00  | £1,196.00 |
| Ply 18 mm, curved ribs, 300 mm deep                        | 20 sheet  | £46.00  | £920.00   |
| Ply 18 mm spreader pads 450 × 450 under every leg          | 7 sheet   | £46.00  | £322.00   |
| <b>C. STEEL</b>                                            |           |         |           |
| Coping tube 60 mm dia, both top edges                      | 40 m      | £18.00  | £720.00   |
| Screw and bolt fixings, coping, ribs to rails, ply to ribs | 1 item    | £620.00 | £620.00   |
| <b>D. BALLAST</b>                                          |           |         |           |
| Ballast to hold the ramp down, see the calc sheet          | 5 t       | £130.00 | £650.00   |

| ITEM                                                               | QUANTITY | RATE              | AMOUNT    |
|--------------------------------------------------------------------|----------|-------------------|-----------|
| Ground anchors, alternative to ballast if the tarmac may be broken | 0 no     | £0.00             | £0.00     |
| <b>E. LABOUR</b>                                                   |          |                   |           |
| Carpenter                                                          | 10 day   | £245.00           | £2,450.00 |
| General labourer                                                   | 4 day    | £185.00           | £740.00   |
| <b>SUMMARY</b>                                                     |          | <b>AMOUNT</b>     |           |
| Materials, steel and ballast                                       |          | £11,089.40        |           |
| Labour                                                             |          | £3,190.00         |           |
| <b>Total, excluding overheads, profit and prelims</b>              |          | <b>£14,279.40</b> |           |
| <b>Rate per metre of ramp</b>                                      |          | <b>£713.97</b>    |           |

**Rates are indicative UK market rates, dated 4 October 2026, there to be challenged.** Excludes overheads, profit, prelims, plant and transport, the design fee, the independent check, the ride inspection regime and the load test, and event insurance.

## 06 Open inputs - nothing is bought or erected until these close

Six things the pack cannot settle on its own.

| OPEN INPUT              | WHY IT MATTERS                                                                                                                               |
|-------------------------|----------------------------------------------------------------------------------------------------------------------------------------------|
| <b>The site</b>         | Wind map value from BS 5975-2 Figure 8 for the location; town or country, altitude, distance to sea. Lock the row and the pressure is fixed. |
| <b>The shape factor</b> | Assumed 1.0 to 1.6. It drives the ballast, and therefore the cost. The designer sets it.                                                     |
| <b>The height</b>       | Adopted 2.00 m because $5.00 = 1.00 \text{ flat} + 2 \times 2.00$ . If it wants to be taller the whole pack re-runs - it is one number.      |
| <b>The ground</b>       | Tarmac assumed. What is beneath decides whether anchors can replace ballast, and that changes the price.                                     |
| <b>Public use</b>       | Whether it is ridden by the public, supervised, or event-only decides which product standard applies and how heavy the inspection regime is. |
| <b>Dynamic loads</b>    | A rider landing on a transition is a dynamic action. Not modelled here at all.                                                               |

## 07 The 3D model, and the documents behind this report

The pack is attached to this report in full.



### The pack

<https://darrenhopwood13-maker.github.io/tw-halfpipe-001/>

<https://darrenhopwood13-maker.github.io/tw-halfpipe-001/>

- **Drawing sheet** — cross section, long elevation, plan, A3 at 1:50 / 1:100 / 1:200
- **Wind and hold-down sheet** — every step, its source, and the ballast sensitivity
- **Priced build sheet** — PDF, Excel and CSV
- **Builder's briefing** — one page: setting out, sequence, call-off, watch-outs
- **3D model** — the ramp as built from this geometry, on a phone

The 3D model is a communication aid: not a structural check, not a design, and not a permit to load or ride.

**instructSite** — Universal Command Prompt for Construction


Silverstream House, 45 Fitzroy Street, London, W1T 6EB | [instructsite.ai](https://instructsite.ai)

Reference TW-HP-001, issued 4 October 2026. Prepared for Darren Hopwood. NOT A DESIGN — NOT FOR CONSTRUCTION — NOT A PERMIT TO LOAD OR RIDE.

TEMPORARY HALF-PIPE SKATE RAMP - SECTION, ELEVATION AND PLAN

Ref TW-HP-001 Rev P01 4 October 2026 All dimensions in metres. 1:50, 1:100, 1:200 at A3

NOT A DESIGN - NOT FOR CONSTRUCTION - NOT A PERMIT TO LOAD

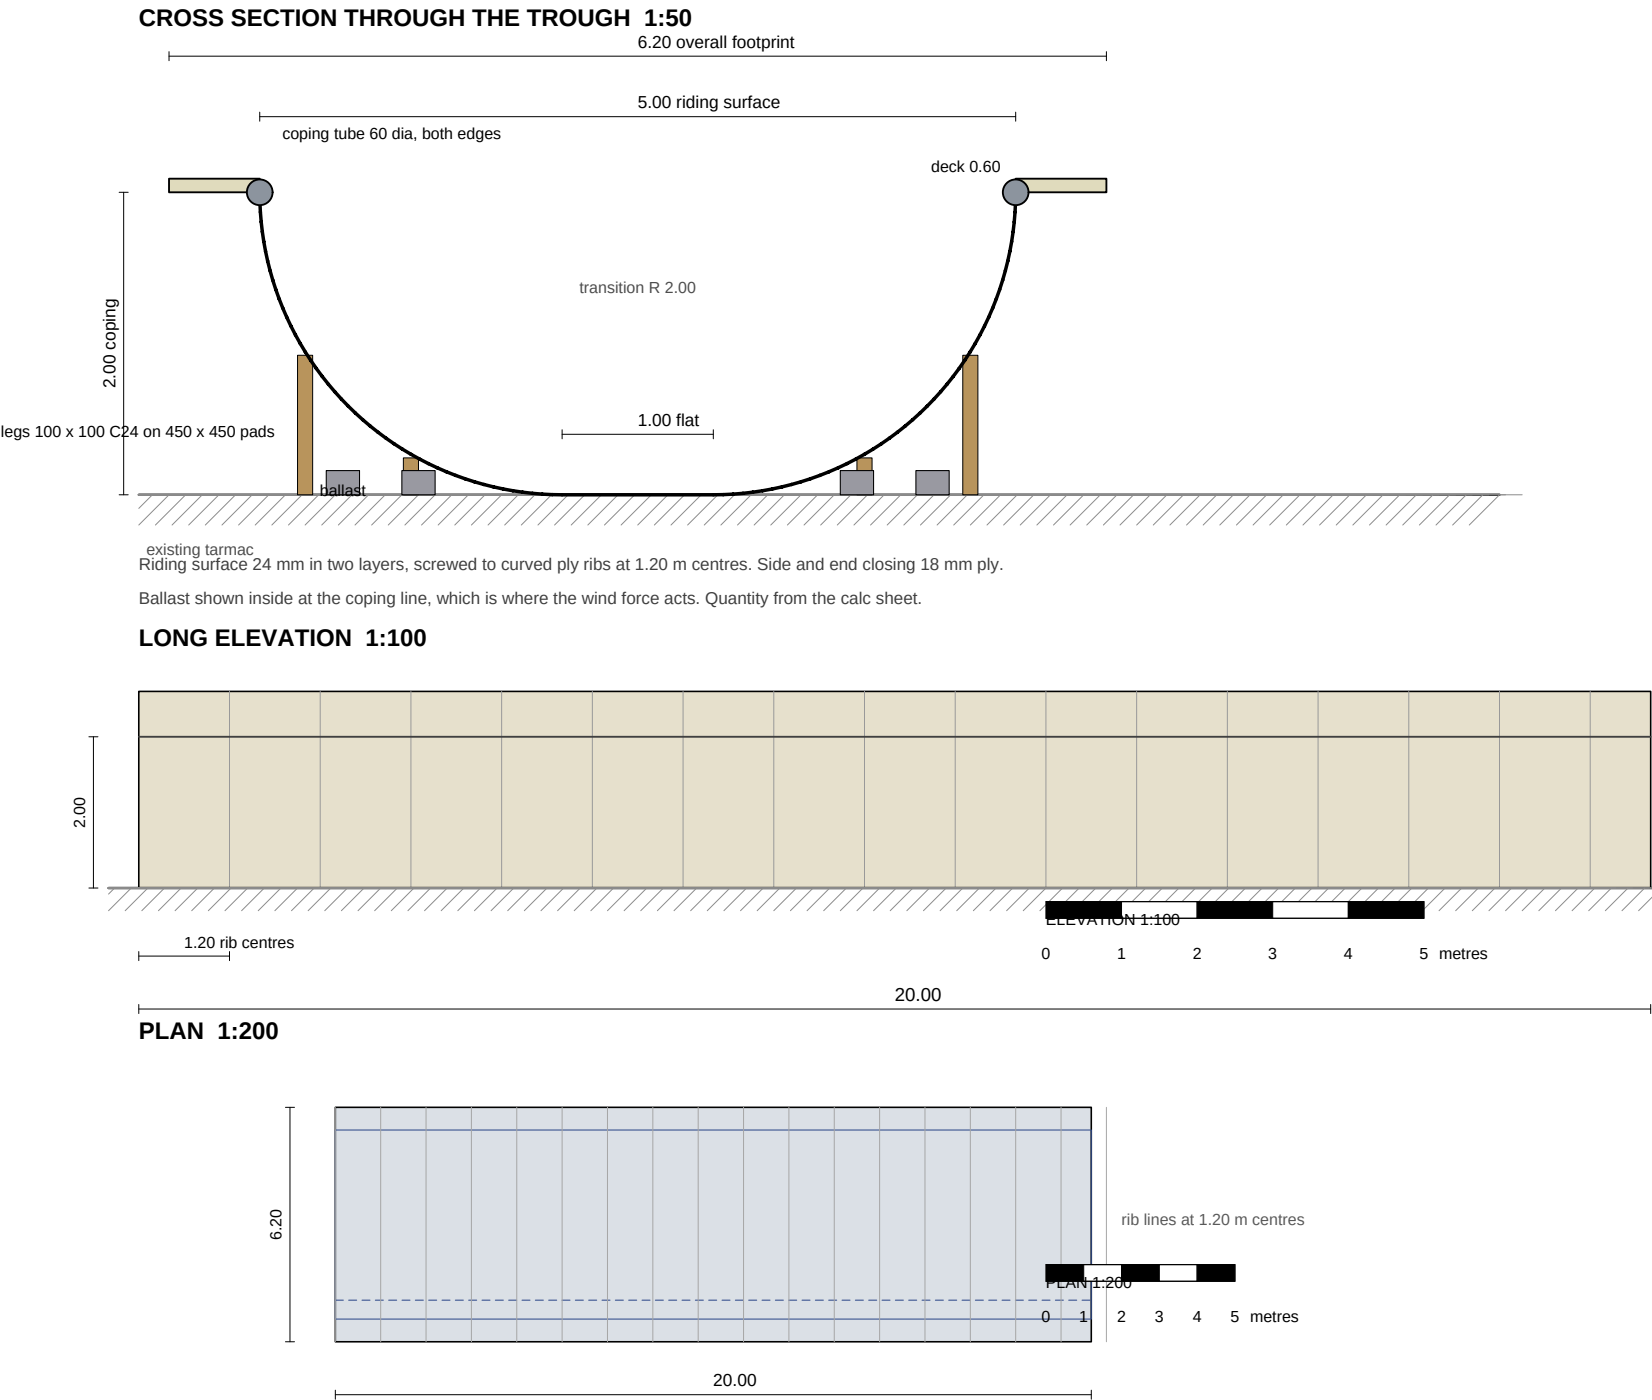

PRINT AT A3 AT 100% - DO NOT SCALE. Where anything differs, the figured dimensions govern,  
not a measurement off the sheet. The scale bar survives reproduction; the ratio does not.

WHAT THIS IS

A temporary half-pipe 20.00 m long with 5.00 m of riding surface: a 1.00 m flat bottom between two 2.00 m transitions, so the coping stands 2.00 m high. Decks 0.60 m each side, 6.20 m overall footprint.

Framing: 100 x 100 C24 legs on 450 x 450 spreader pads, 100 x 75 bearers laid flat, curved ply ribs at 1.20 m centres, 24 mm ply riding surface in two layers.

IT HAS TO BE HELD DOWN. The ramp presents a 40 m2 face to the wind - ballast in the order of 3 to 7 tonnes, or ground anchors. See the calc sheet. Nothing is ridden until that is designed, checked and permitted.

THE STANDARDS THAT GOVERN IT

BS EN 14974:2019

Skateparks - safety requirements and test methods. THE product standard for a facility used by the public on skateboards, roller sports and BMX. Supersedes BS EN 14974:2006+A1:2010.

BS EN 13814-1:2019+A1:2024

Safety of amusement rides and amusement devices - design and manufacture. Applies to mobile and temporary devices: if the ramp is hired in as an attraction this is the design standard.

BS EN 1991-1-4

Wind actions, where the designer works to Eurocode rather than the simplified method.

BS 5975-1:2024 / BS 5975-2:2024

Temporary works procedure: roles, register, check categories, permits. Replaced BS 5975:2019.

CDM 2015

Principal Contractor duties, the design brief, and the temporary works register.

BS EN 1090-1

Execution of steel structures - if the coping, anchors or frame are fabricated steel.

Nothing is erected, ballasted or ridden until a competent temporary works designer has designed and checked it and a permit to load is issued.

| SECTION, ELEVATION, PLAN                                   |                                | Rev P01 |
|------------------------------------------------------------|--------------------------------|---------|
| Project                                                    | Temporary half-pipe skate ramp |         |
| Drawing                                                    | 1 of 1                         |         |
| Reference                                                  | TW-HP-001                      |         |
| Date                                                       | 4 October 2026                 |         |
| Drawn                                                      | Banksy, for Dal Hopwood        |         |
| Scale                                                      | 1:50, 1:100, 1:200 at A3       |         |
| NOT FOR CONSTRUCTION - NOT A DESIGN - NOT A PERMIT TO LOAD |                                |         |

# TEMPORARY HALF-PIPE RAMP - WIND AND HOLD-DOWN

Ref TW-HP-001 Rev P01 4 October 2026 | Banksy, for Dal Hopwood

NOT A DESIGN - NOT FOR CONSTRUCTION - NOT A PERMIT TO LOAD

## 1. WHAT THIS IS

NOT A DESIGN - NOT FOR CONSTRUCTION - NOT A PERMIT TO LOAD OR RIDE.

The wind pressure is calculated and every step is shown. The STRUCTURE is not designed here.

The design and its independent check must be produced, checked and OWNED by a competent

temporary works designer, with the structural verification to the governing standards below.

Nothing is erected, ballasted or ridden until a permit to load has been issued.

It calculates the wind pressure at the site and what it does to a 20 m ramp, and it sets out the hold-down demand. It does NOT design the structure, the transitions or the connections, and it does not cover the loads a skateboarder puts into it.

## 2. THE STRUCTURE AND THE BASIS

|               |                                                                              |
|---------------|------------------------------------------------------------------------------|
| Item          | Temporary half-pipe, 20.00 m long, 5.00 m riding surface, coping 2.00 m high |
| Cross section | 1.00 m flat bottom + two 2.00 m transitions, decks 0.60 m each side          |
| Footprint     | 20.00 m x 6.20 m overall                                                     |
| Exposure      | EXTERNAL and open to the sky - a full wind case applies                      |
| Setting       | town assumed; the site is not confirmed                                      |
| Duration      | cprob = 1.0 (more than one year)                                             |
| Wind area     | 40.0 m2 across the length - the ramp is a sail                               |

## 3. WIND PRESSURE - AND WHY THIS IS THE POINT OF THE WHOLE PACK

Dynamic pressure  $q_p = 0.613 \times c_{prob}^2 \times C_{ef} \times S_{wind}^2$ , with  $S_{wind}$  and  $C_{ef}$  taken from the validated TWf2012:01 calculator that reproduces the published worked example. Those two are properties of the SITE and the HEIGHT only - they do not depend on what is being checked, so they carry across to a ramp. The hoarding's shape coefficients do NOT, and are not used here.

| vb,map | from sea | Cef   | Swind | qp kN/m2 |
|--------|----------|-------|-------|----------|
| 22 m/s | 2 km     | 1.070 | 22.44 | 0.330    |
| 22 m/s | 30 km    | 0.994 | 22.44 | 0.307    |
| 25 m/s | 2 km     | 1.070 | 25.50 | 0.427    |
| 25 m/s | 30 km    | 0.994 | 25.50 | 0.396    |

Governing for what follows:  $q_p = 0.427 \text{ kN/m}^2$ , the worst row. The range is shown because the site is not yet confirmed.

#### 4. WHAT THE WIND DOES TO IT

The ramp presents its 40 m<sup>2</sup> side elevation to a cross wind - 20.00 m long by 2.00 m high. The horizontal force is  $q_p \times C_f \times A$ .  $C_f$  is NOT from any standard I hold: it is assumed, and carried as a sensitivity so the designer can see what their own figure costs.

| Cf assumed | wind force kN | sliding resist. at mu 0.30 kN | extra ballast t | verdict |
|------------|---------------|-------------------------------|-----------------|---------|
| 1.0        | 18.7          | 62.4                          | 3.0             | ballast |
| 1.3        | 24.3          | 81.1                          | 4.9             | ballast |
| 1.6        | 30.0          | 99.8                          | 6.8             | ballast |

Self weight is about 3.4 t (ply, timber, rib plates), which at  $\mu = 0.30$  resists about 10 kN on its own - so the ramp needs holding down on top of its own weight in every case. That is the commercial headline: ballast in the order of 3 to 7 tonnes, or ground anchors, before anyone rides it.

Uplift is not calculated here. A trough is open on top: wind over the opening can lift the surface, and wind getting under an unclosed side can do worse. Both are the designer's checks - the closed sides shown on the sheet are there precisely so wind cannot get inside.

#### 5. THE STANDARDS THAT GOVERN IT

BS EN 14974:2019 Skateparks - safety requirements and test methods. THE product standard for a facility used by the public on skateboards, roller sports and BMX. Supersedes BS EN 14974:2006+A1:2010.

BS EN 13814-1:2019+A1:2024 Safety of amusement rides and amusement devices - design and manufacture. Applies to mobile and temporary devices: if the ramp is hired in as an attraction this is the design standard.

BS EN 1991-1-4 Wind actions, where the designer works to Eurocode rather than the simplified method.

BS 5975-1:2024 / BS 5975-2:2024 Temporary works procedure: roles, register, check categories, permits. Replaced BS 5975:2019.

CDM 2015 Principal Contractor duties, the design brief, and the temporary works register.

BS EN 1090-1 Execution of steel structures - if the coping, anchors or frame are fabricated steel.



## 6. NOT APPLICABLE, SAID OUT LOUD

---

- The Temporary Works Forum hoarding guide (TWf2012:01) does NOT govern this. Only its wind pressure route is borrowed, and said so above.

- Building Regulations do not govern a temporary ramp.

- Highways Act 1980 s.169 does not apply if the ramp is inside a car park or yard.

## 7. OPEN INPUTS - NOTHING IS BOUGHT OR ERECTED UNTIL THESE CLOSE

---

1. THE SITE. The wind map value comes from BS 5975-2 Figure 8 for the actual location; the

range above is shown because the site is not confirmed. Also: town or country, altitude,

and distance to the sea.

2. THE SHAPE FACTOR. Not taken from any standard I have. It is assumed and carried as a

sensitivity - 1.0 to 1.6 covers the range. The designer sets it, and it drives the ballast.

3. THE HEIGHT. Adopted 2.00 m to the coping, because  $5.00\text{ m} = 1.00\text{ flat} + 2 \times 2.00\text{ transition}$ .

If Dal wants a different height the whole pack re-runs - it is one number.

4. THE GROUND. Tarmac assumed. What is under it decides whether ground anchors are viable

instead of ballast, and it changes the price.

5. PUBLIC USE. Whether this is ridden by the public, supervised, or event-only, decides which

of the two product standards applies and how heavy the inspection regime is.

6. DYNAMIC LOADS. A skateboarder landing on a transition is a dynamic action. Not modelled

here at all - the designer's to derive.

**A wind check is not a permit to load. A ramp is not ridden until the design, the hold-down and the ride inspection have been signed off.**

# TEMPORARY HALF-PIPE RAMP - PRICED BUILD SHEET

Ref TW-HP-001   Rev P01   4 October 2026

NOT A DESIGN - NOT FOR CONSTRUCTION - NOT A PERMIT TO LOAD

Indicative UK supply rates, 4 October 2026, delivered. Excludes overheads, profit, prelims, plant, the design fee, the independent check, the ride inspection regime, and the event insurance.

| Description                                                                                                                                       | Qty | Unit  | Rate   | Amount           |
|---------------------------------------------------------------------------------------------------------------------------------------------------|-----|-------|--------|------------------|
| <b>A. TIMBER</b>                                                                                                                                  |     |       |        |                  |
| Leg 100 x 100 C24 treated, average 1.50 m<br>2 per cross frame, both sides. Length varies with the transition                                     | 36  | no    | 16.50  | 594.00           |
| Bearer / rail 100 x 75 C24 treated, laid flat<br>9 runs x 20 m: 3 under the flat, 3 up each transition                                            | 180 | m     | 8.20   | 1,476.00         |
| Cross bearer under the flat, 100 x 75<br>18 frames x 1.5 m across the flat bottom                                                                 | 27  | m     | 8.20   | 221.40           |
| <b>B. PLY</b>                                                                                                                                     |     |       |        |                  |
| Ply 12 mm exterior, riding surface, two layers<br>146 m2 surface + 24 m2 deck, doubled = 340 m2, plus cutting waste                               | 115 | sheet | 38.00  | 4,370.00         |
| Ply 18 mm exterior, side and end closing<br>About 76 m2 closing so nobody can get inside the structure                                            | 26  | sheet | 46.00  | 1,196.00         |
| Ply 18 mm, curved ribs, 300 mm deep<br>36 ribs in two segments each, nested 4 segments per sheet                                                  | 20  | sheet | 46.00  | 920.00           |
| Ply 18 mm spreader pads 450 x 450 under every leg<br>36 pads, cut from 7 sheets                                                                   | 7   | sheet | 46.00  | 322.00           |
| <b>C. STEEL</b>                                                                                                                                   |     |       |        |                  |
| Coping tube 60 mm dia, both top edges<br>2 x 20 m, with end caps and fixings to the deck                                                          | 40  | m     | 18.00  | 720.00           |
| Screw and bolt fixings, coping, ribs to rails, ply to ribs<br>Allowance: about 4,000 screws at 150 c/c plus M10 bolts                             | 1   | item  | 620.00 | 620.00           |
| <b>D. BALLAST</b>                                                                                                                                 |     |       |        |                  |
| Ballast to hold the ramp down, see the calc sheet<br>5 t in the middle of the 3.0-6.8 t range. Concrete blocks or water ballast                   | 5   | t     | 130.00 | 650.00           |
| Ground anchors, alternative to ballast if the tarmac may be broken<br>Priced as nil. Cheaper if the ground allows - CHECK before ordering ballast | 0   | no    | 0.00   | 0.00             |
| <b>E. LABOUR</b>                                                                                                                                  |     |       |        |                  |
| Carpenter<br>2 carpenters x 5 days: cut ribs, frame, deck, surface, closing                                                                       | 10  | day   | 245.00 | 2,450.00         |
| General labourer<br>Assisting, handling sheets, ballast                                                                                           | 4   | day   | 185.00 | 740.00           |
| Materials, steel and ballast                                                                                                                      |     |       |        | 11,089.40        |
| Labour                                                                                                                                            |     |       |        | 3,190.00         |
| <b>TOTAL - excludes overheads, profit and prelims</b>                                                                                             |     |       |        | <b>14,279.40</b> |
| <b>Rate per metre of ramp (20 m long)</b>                                                                                                         |     |       |        | <b>713.97</b>    |

## WHAT THE PRICE DOES NOT INCLUDE

- Overheads, profit and prelims. Plant and transport of a 20 m structure.
- The temporary works design and its independent check - that is the designer's fee.
- The ride inspection regime and the load test required before it opens to the public.
- Event insurance, supervision, marshalling, or the site's own traffic management.
- Ground anchors: priced at nil, because if the ground allows them they replace the ballast.
- Any change if the site comes back inland, or the shape factor lands higher than assumed.

Rates are indicative. Replace them with the rate book before this is used commercially.

# TEMPORARY HALF-PIPE RAMP - BUILDER'S BRIEFING

Ref TW-HP-001 Rev P01 4 October 2026 One page. Full details on the drawings.

**NOT A DESIGN - NOT FOR CONSTRUCTION - NOT A PERMIT TO LOAD**

**NOT A DESIGN and NOT FOR CONSTRUCTION.** The temporary works designer owns the design and its independent check. Do

not erect, ballast or let anyone ride it until a permit to load has been issued.

## WHAT YOU ARE BUILDING

---

A temporary half-pipe 20.00 m long with 5.00 m of riding surface: a 1.00 m flat bottom between two 2.00 m transitions, coping 2.00 m high, 0.60 m decks behind each coping, 6.20 m overall. Timber framing, 24 mm ply surface in two layers, closed sides.

## SETTING OUT - DO THIS FIRST

---

- Set out the 20.00 m length and the 6.20 m width. Check the diagonals.
- Mark the coping lines and the 1.00 m flat bottom, then mark every cross frame at 1.20 m centres - 18 of them.
- Set the flat bottom and the two transitions out with a trammel from the transition centres. A transition that is not a true arc will ride badly and will be rejected.

## BUILD SEQUENCE

---

1. Spreader pads first, 450 x 450, under every leg. Legs are 100 x 100 C24 and their height follows the transition - do not cut them all the same length.
2. Fix the longitudinal bearers, then the curved ribs at 1.20 m centres. Check every arc against the trammel before you board over it.
3. Lay the 24 mm surface in two layers, screwed at 150 mm centres, joints staggered between layers and landing on a rib.
4. Fix the coping tube along both top edges, then the decks.
5. Close the ends and the sides with 18 mm ply. Nothing must be reachable inside the structure - that is both a safety point and how the wind check assumes it behaves.
6. Ballast last, to the design quantity and position. Do not ride it before that is done and signed off.

## CALL OFF

---

- Leg 100 x 100 C24 treated, average 1.50 m - 36 no
